


STRATEGIC ALIGNMENT & OPERATIONAL READINESS

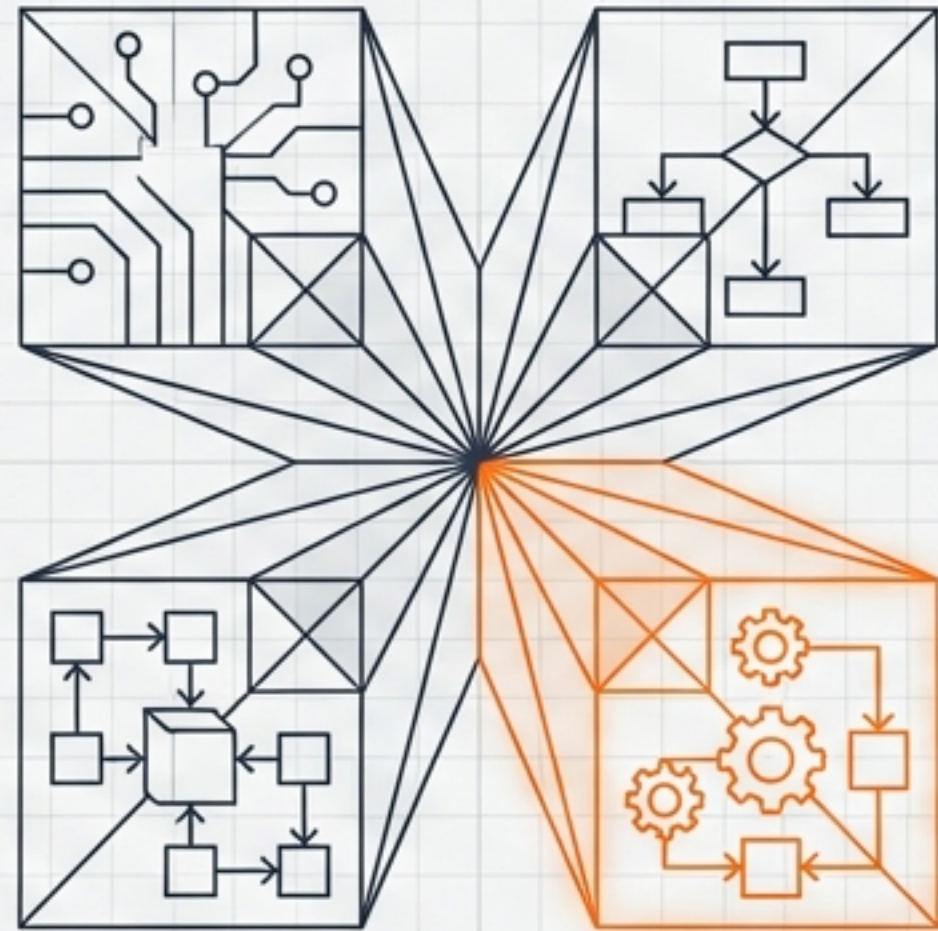

Sentraais Cut-Over | Operating Model Implementation | March 15 Target

INTERNAL LEADERSHIP / STEERCO ONLY

UPDATED: 2026-02-07

STATUS: CONFIDENTIAL

THE MISSION

Stabilize, build, and launch the new Sentrais entity by March 15, 2026.

The core objective is to transition to the Four-Zone Operating Model, strictly separating Data Sovereignty from Commercial Execution.

WEEKS 1-6

**INFRASTRUCTURE
& IDENTITY**

WEEKS 6-8

**HARDENING
& UAT**

MARCH 15


FULL CUT-OVER

DECISION GATE

Success requires passing the Go/No-Go readiness checklist: Governance, Security, Platform, Brand.

TARGET STATE: FOUR-ZONE OPERATING MODEL

Balancing Sovereignty and Execution

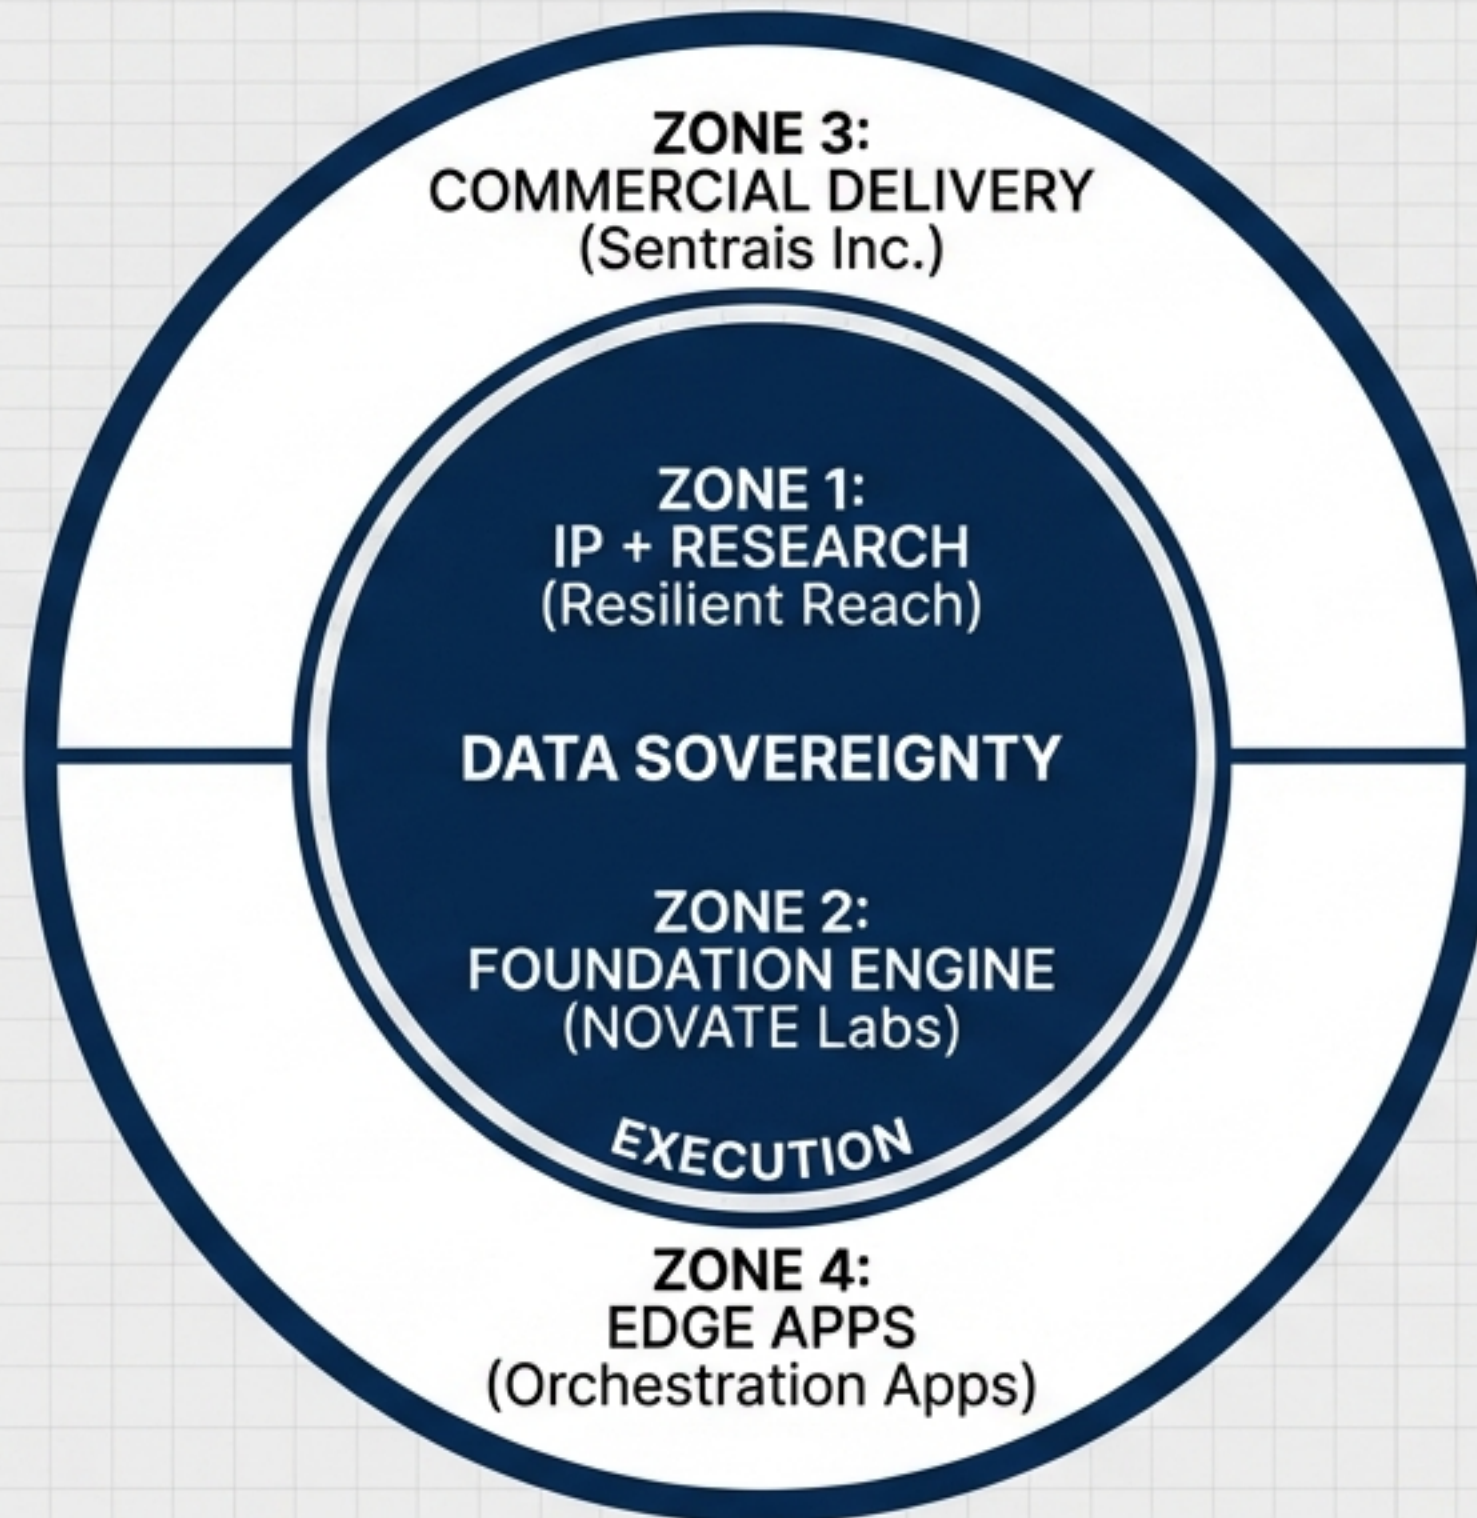

KEY INSIGHT: Separates the CREATION of value (Zones 1-2) from the DELIVERY of value (Zones 3-4). Ensures IP resilience while enabling commercial scale.

DEEP DIVE: ZONES 1 & 2 (SOVEREIGNTY)

Establishing the foundation for IP ownership and innovation.



ZONE 1: IP + RESEARCH (Resilient Reach)

ROLE: The Legislative Branch
(Rules & Standards)

MANDATE: Own the models, NIN method, ingestion patterns, Evidence Ledger specifications, and reference architectures.


ZONE 2: FOUNDATION ENGINE (NOVATE Labs)

ROLE: The Laboratory (Experimentation)

MANDATE: R&D and innovation programs, research studies, Proof of Concepts (POCs) under MOU, and community activation.

DEEP DIVE: ZONES 3 & 4 (EXECUTION)

Driving commercial delivery and edge orchestration.

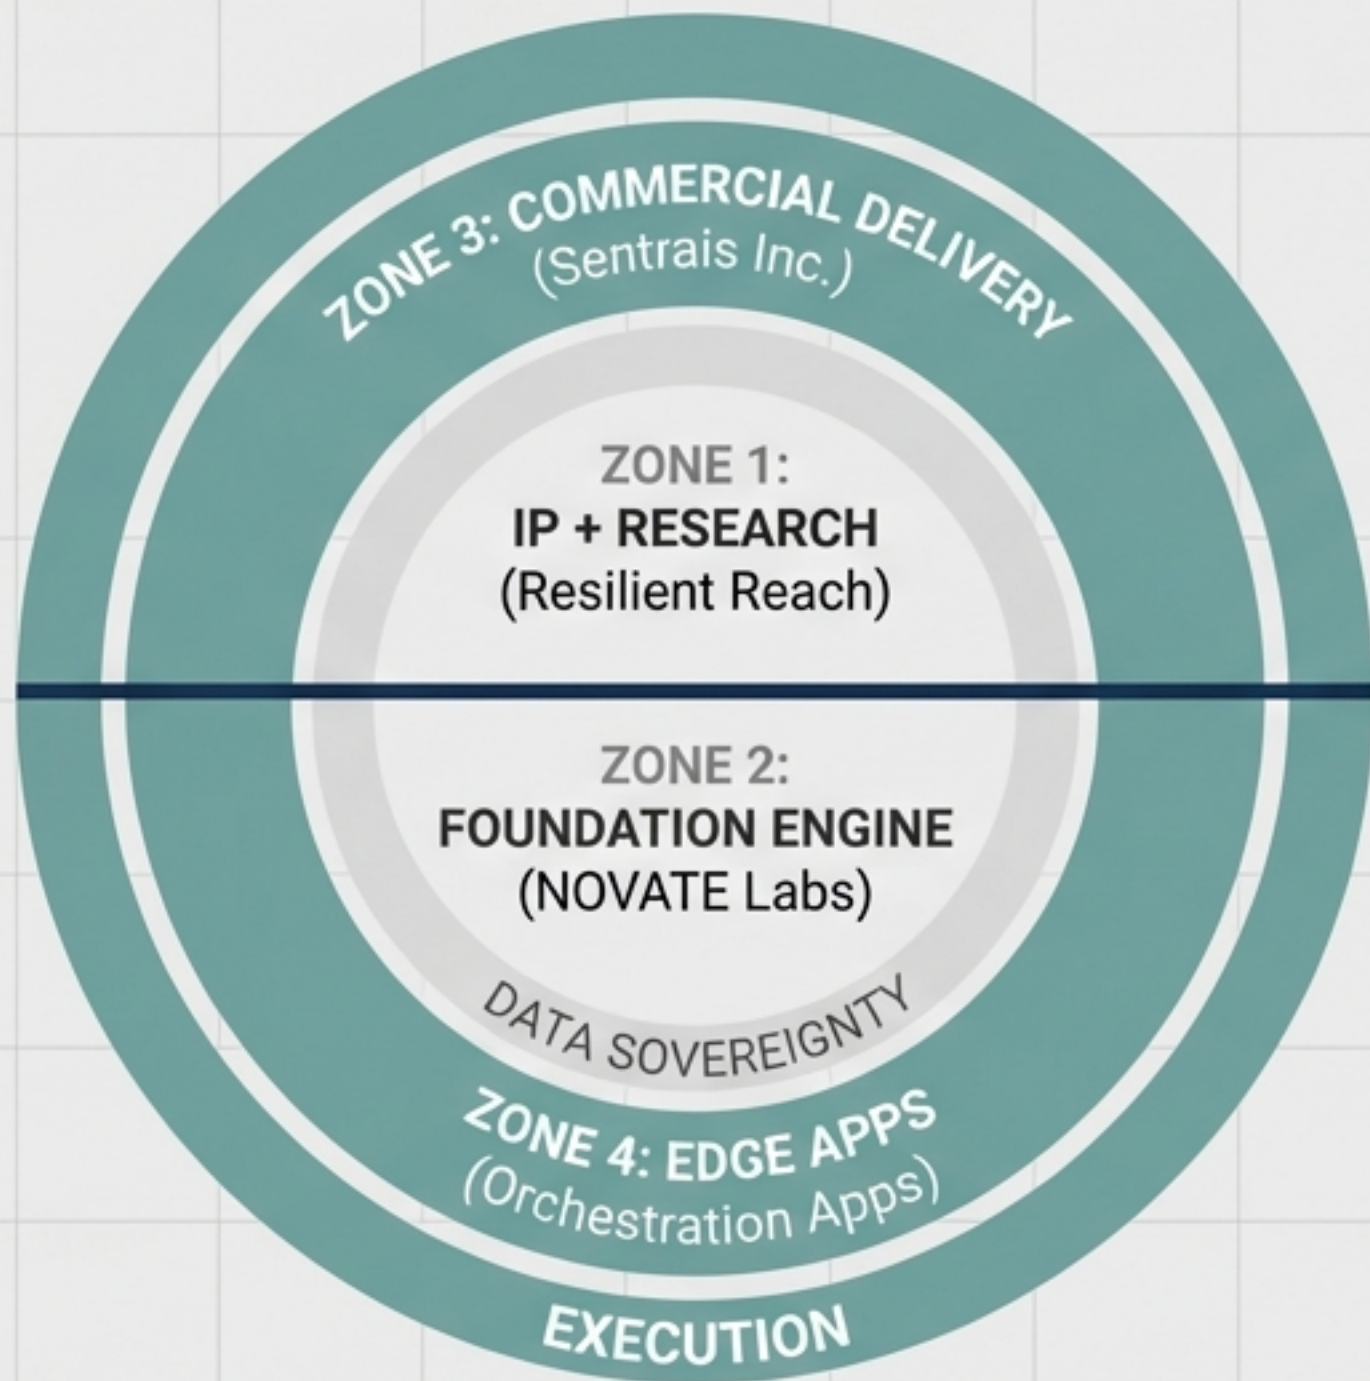

ZONE 3: COMMERCIAL DELIVERY (Sentrais Inc.)


- **ROLE:** The Commercial Engine (Monetization)
- **MANDATE:** Client contracts, licensing, managed services, platform runtime, and delivery governance.

ZONE 4: EDGE APPS (Orchestration Apps)

- **ROLE:** The Product (User-Facing)
- **MANDATE:** Specific application deployment including Blueprint360, EVERGAME, eVenu, CiviGrid, SEAR engines, and Live Intelligence modules.


BLUEPRINT360 (NIN) EXECUTION FLOW

Standardizing the path from Forensics to Scale.

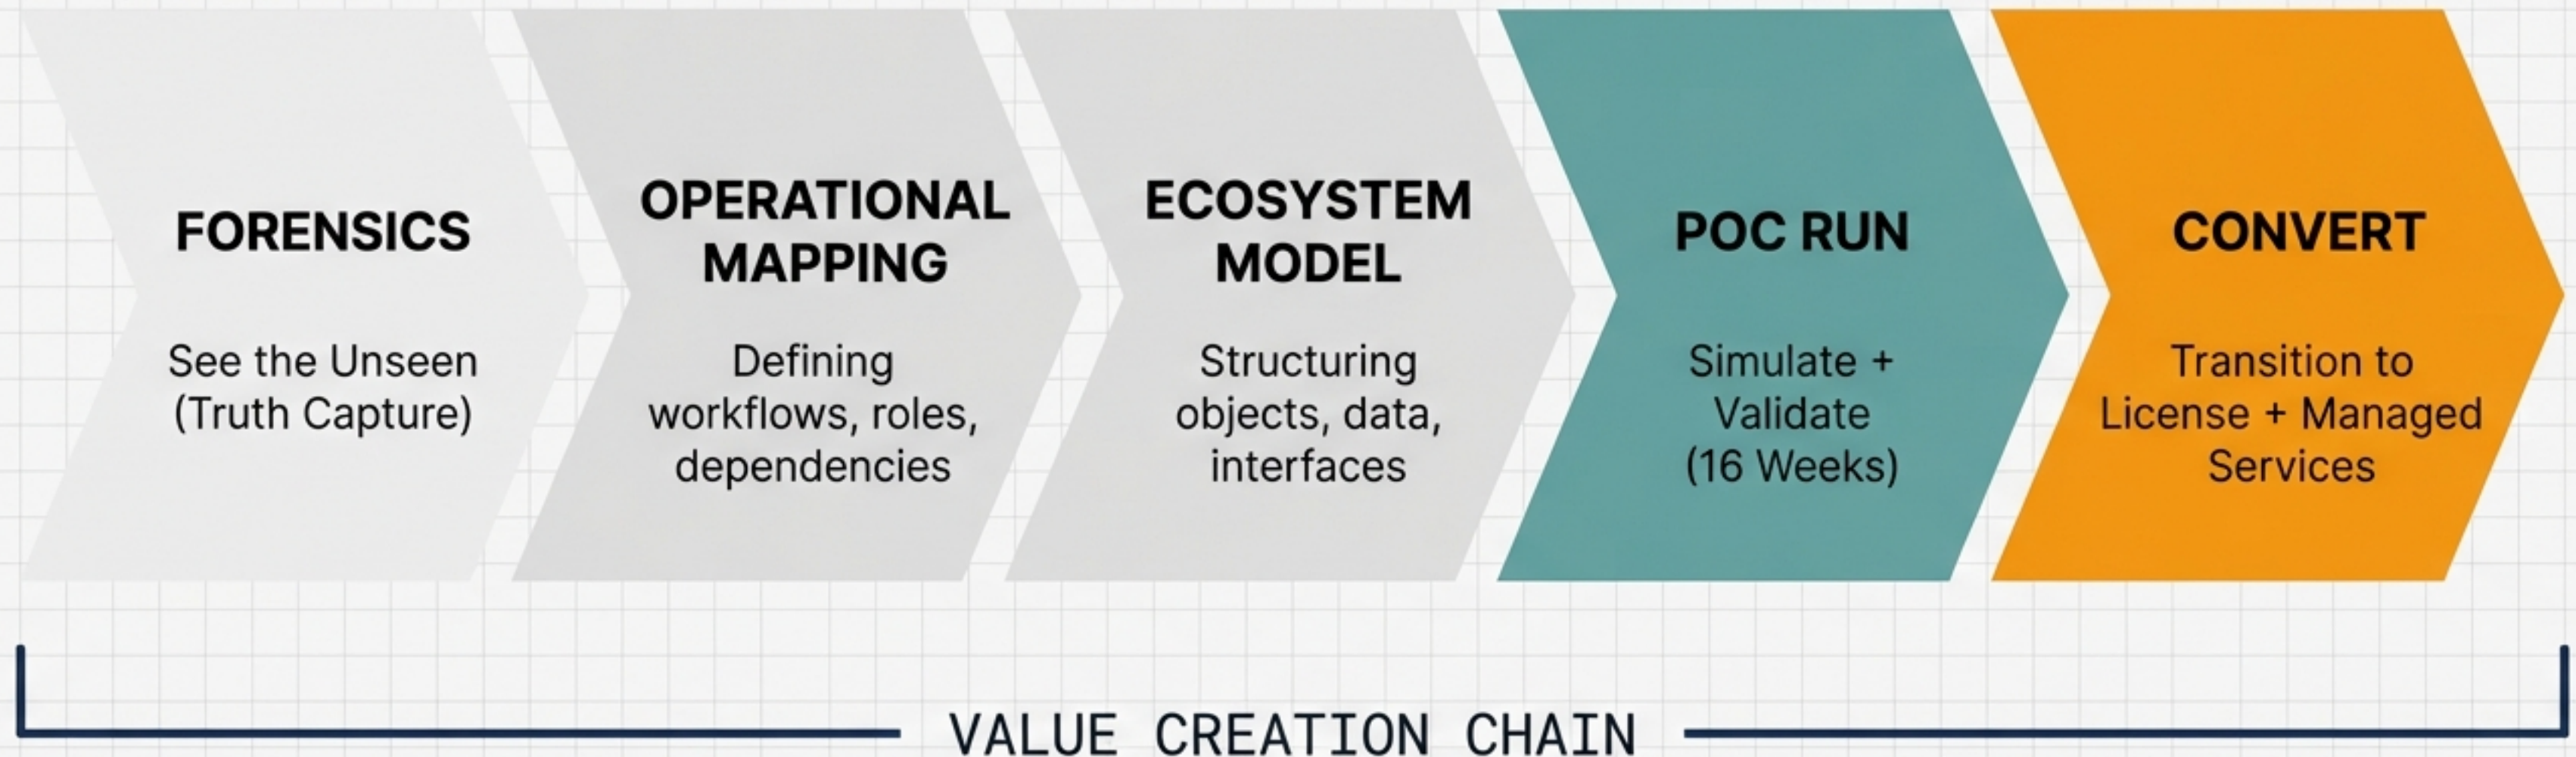

THE ROAD TO MARCH 15

Four-phase sequence: Stabilize, Build, Harden, Cut-Over.

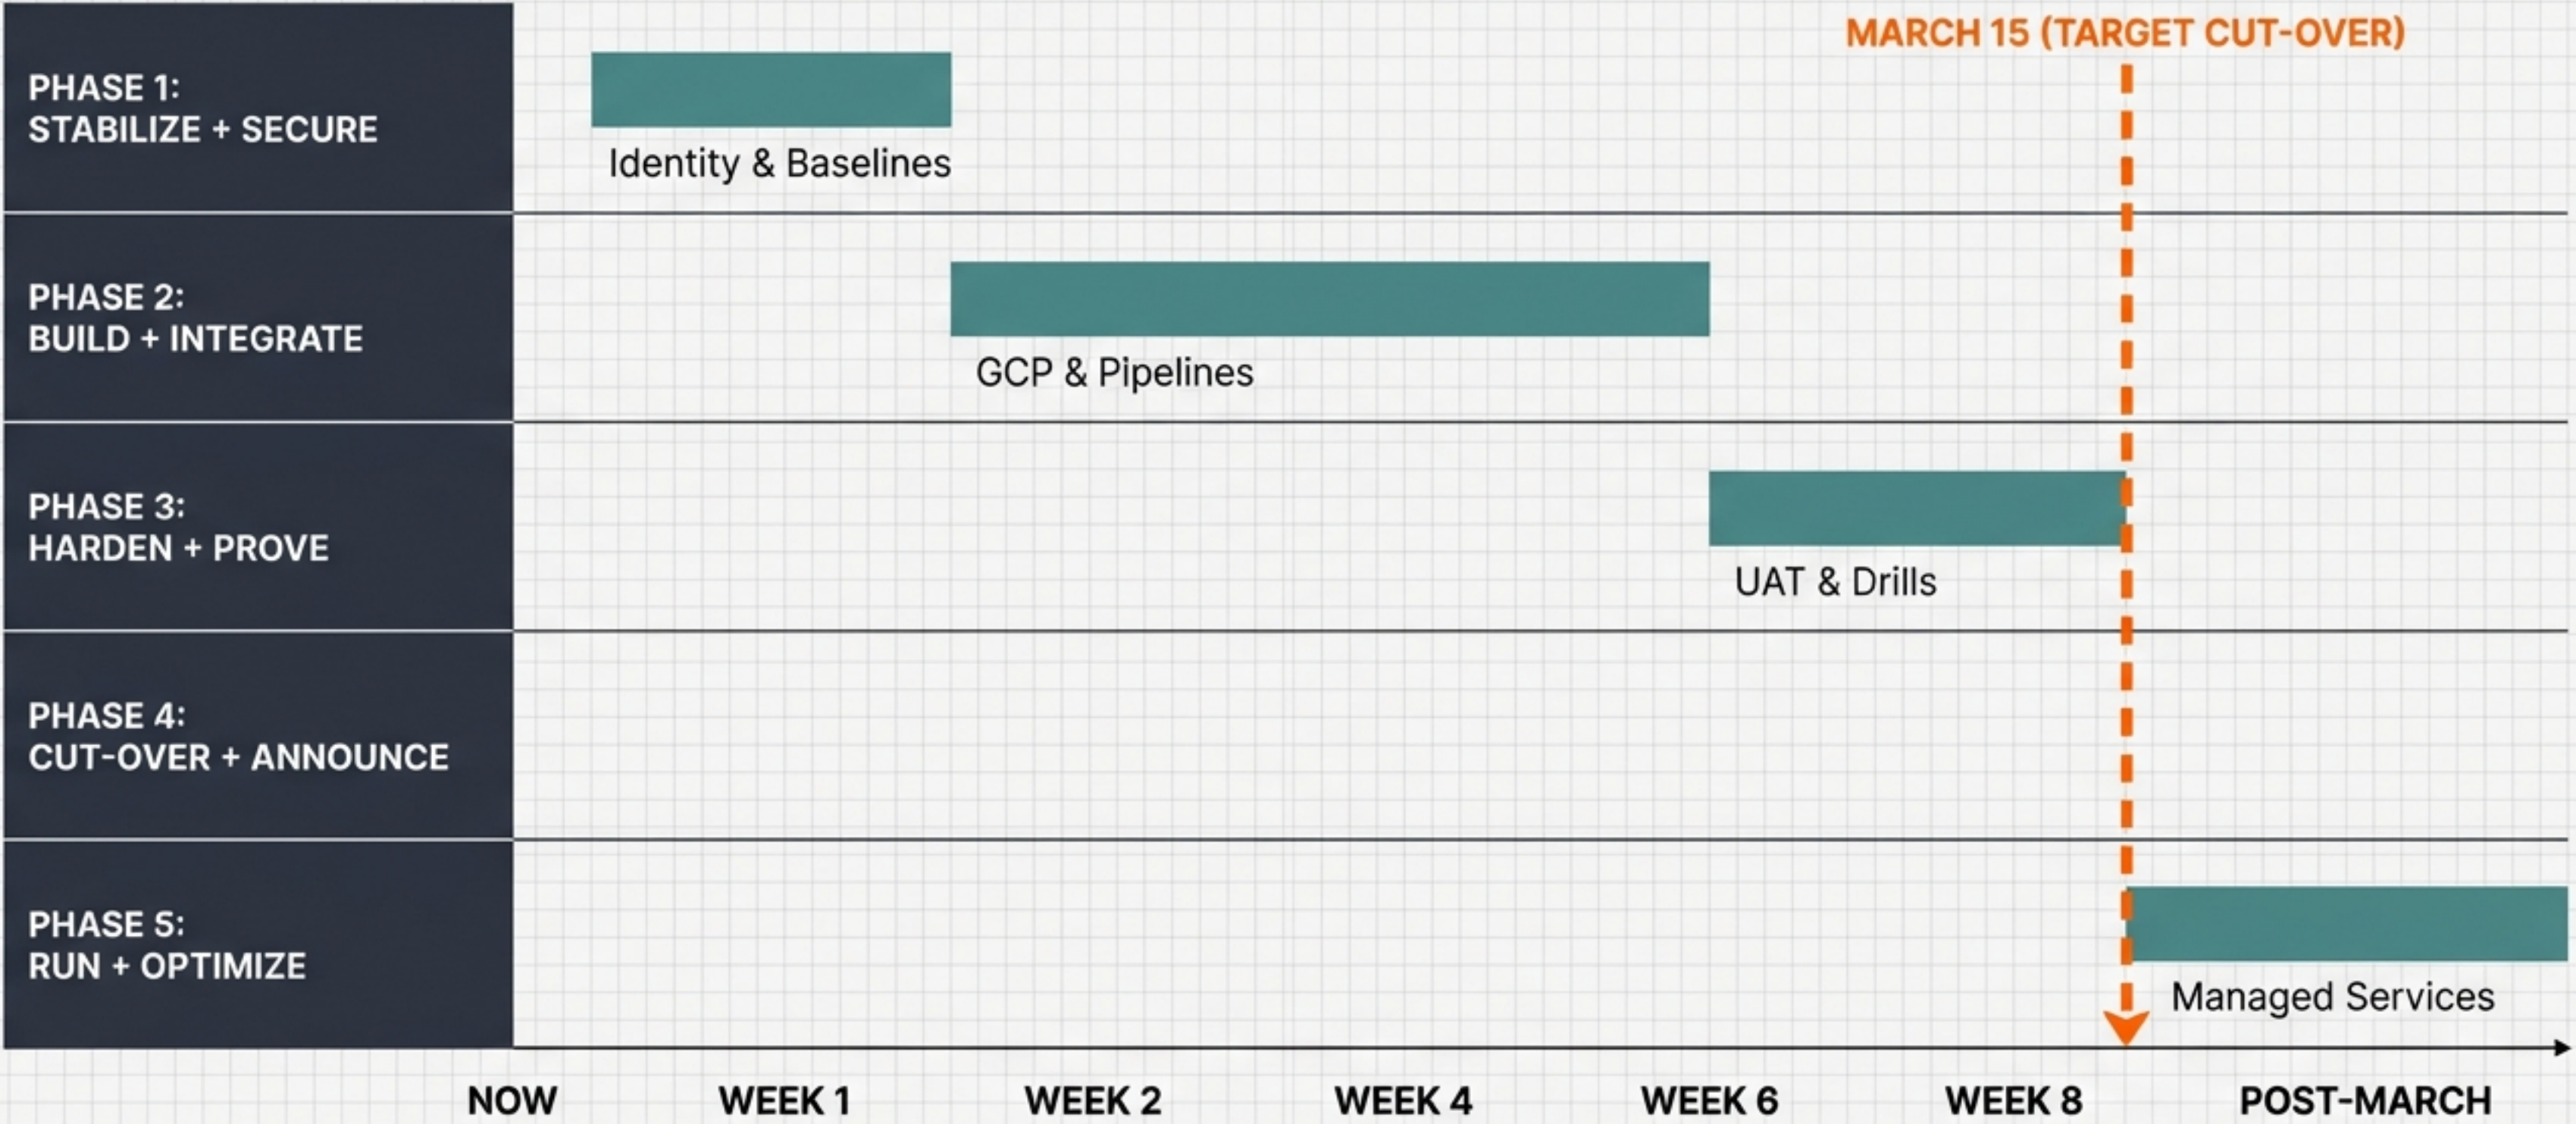

WEEKS 1-6 DETAIL: STABILIZE & BUILD

Infrastructure stabilization and core integration.

PHASE 1 (WEEKS 1-2): STABILIZE + SECURE

- **IDENTITY:** Consolidate identity and access control.
- **ENDPOINTS:** Secure home networks and establish baseline policies.

IN PROGRESS

PHASE 2 (WEEKS 2-6): BUILD + INTEGRATE

- **CLOUD SETUP:** GCP setup including core objects and ingestion pipelines.
- **INTEGRATION:** Launch integration for the Challenge.

NEXT UP

WEEKS 6-8 DETAIL: HARDEN & LAUNCH

Prioritizing verification, drills, and final cut-over. Inter Regular

MARCH 15 (TARGET CUT-OVER)



PHASE 3 (WEEKS 6-8): HARDEN + PROVE

- **VALIDATION:** UAT and Evidence Ledger checks.
- **DRILLS:** Runbooks and incident response simulations.

IN PROGRESS



PHASE 4 (MARCH 15): CUT-OVER + ANNOUNCE

- **TECH:** Domain cut-over and SOR (System of Record) systems locked.
- **BRAND:** Brand cut-over and operational cadence locked.

TARGET

MARCH 15 (TARGET CUT-OVER)

READINESS REQUIREMENT 1: GOVERNANCE

Establishing accountability and decision rights.



STEERCO CADENCE

Locked weekly. Decision owners identified for NFL Challenge, Platform, and Security.



RACI CHART

Published and active for Tye, Ryan, Mikalina, Kirby, Erin, Knox, and Tiana (plus escalation path).



SOURCE OF TRUTH

OneNote/SharePoint structure established with dated artifacts and intake workflow.

STATUS: REQUIRED FOR GO/NO-GO

READINESS REQUIREMENT 2: SECURITY BASELINE

Non-Negotiable Requirements.

ENDPOINTS



- Protection deployed to all devices.
- MDM baseline configured.
- Admin rights minimized.

ACCESS



- SSO/MFA enforced for Google Workspace, cloud consoles, and core SaaS.
- Password vault adopted.

NETWORK



- Home network hardened: Secure Wi-Fi, monitored gateway, VPN posture for travel.

RESPONSE




- Incident response runbook defined: Who to call, containment steps, evidence capture, comms.

READINESS REQUIREMENT 3: PLATFORM & CLOUD

Infrastructure validation and pipeline integrity.

- ☐ **GCP FOUNDATIONS:** Org/project structure, IAM, logging, billing controls, and backup strategy established.
- ☐ **DATA PIPELINES:** Ingestion pipeline tested on 2+ datasets (NFL SOPs or challenge artifacts) with mapping QA.
- ☐ **ENVIRONMENT:** Sandbox and production separation confirmed. Least-privilege access for vendors/contractors.

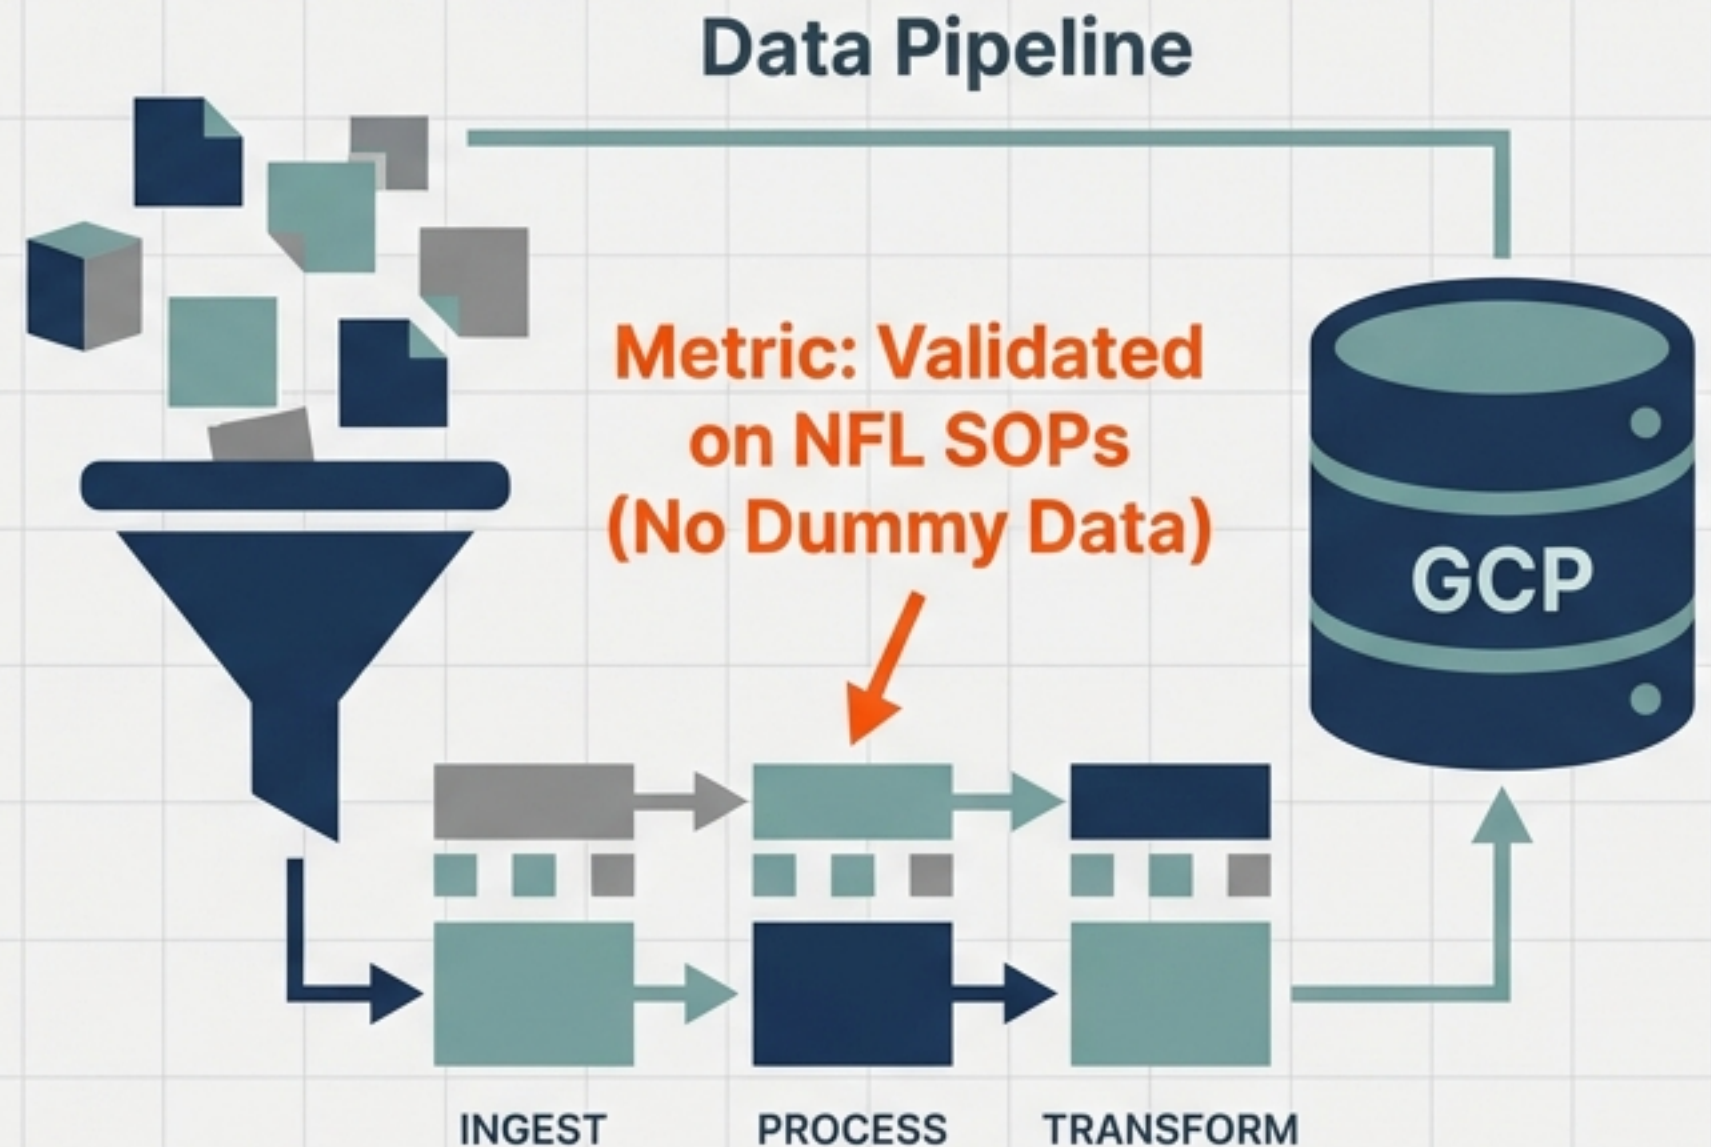

READINESS REQUIREMENT 4: NFL NFL CHALLENGE

Launch enablement for primary commercial driver.

PLANNING

- Updated SOW timeline reflected in project plan.
- Integration plan for Pitchtape (or equivalent) finalized.

TESTING

- UAT plan, test users, and feedback loop in place.
- Defect triage process defined.

EXECUTION

- Run-of-show for launch agreed, including comms, support coverage, and escalation paths.

READINESS REQUIREMENT 5: BRAND & CUT-OVER

External execution and market alignment.

DIGITAL ASSETS

Entity and domain cut-over plan finalized. Redirects, email routing, signatures, key artifacts ready.

PARTNER NARRATIVE

Aligned story: Sentrais as the “OS”, Blueprint360 as the “POC Engine”, and Edge Apps as “Deployments”.


LAUNCH KIT

Announcement materials ready for Mar 14-15: 1-pager, website landing, sponsor list, invite strategy.

CRITICAL: CONSISTENCY IN “SENTRAI AS OS” NARRATIVE.

POST-LAUNCH: RUN + OPTIMIZE

Day 2 Operations and Continuous Improvement.

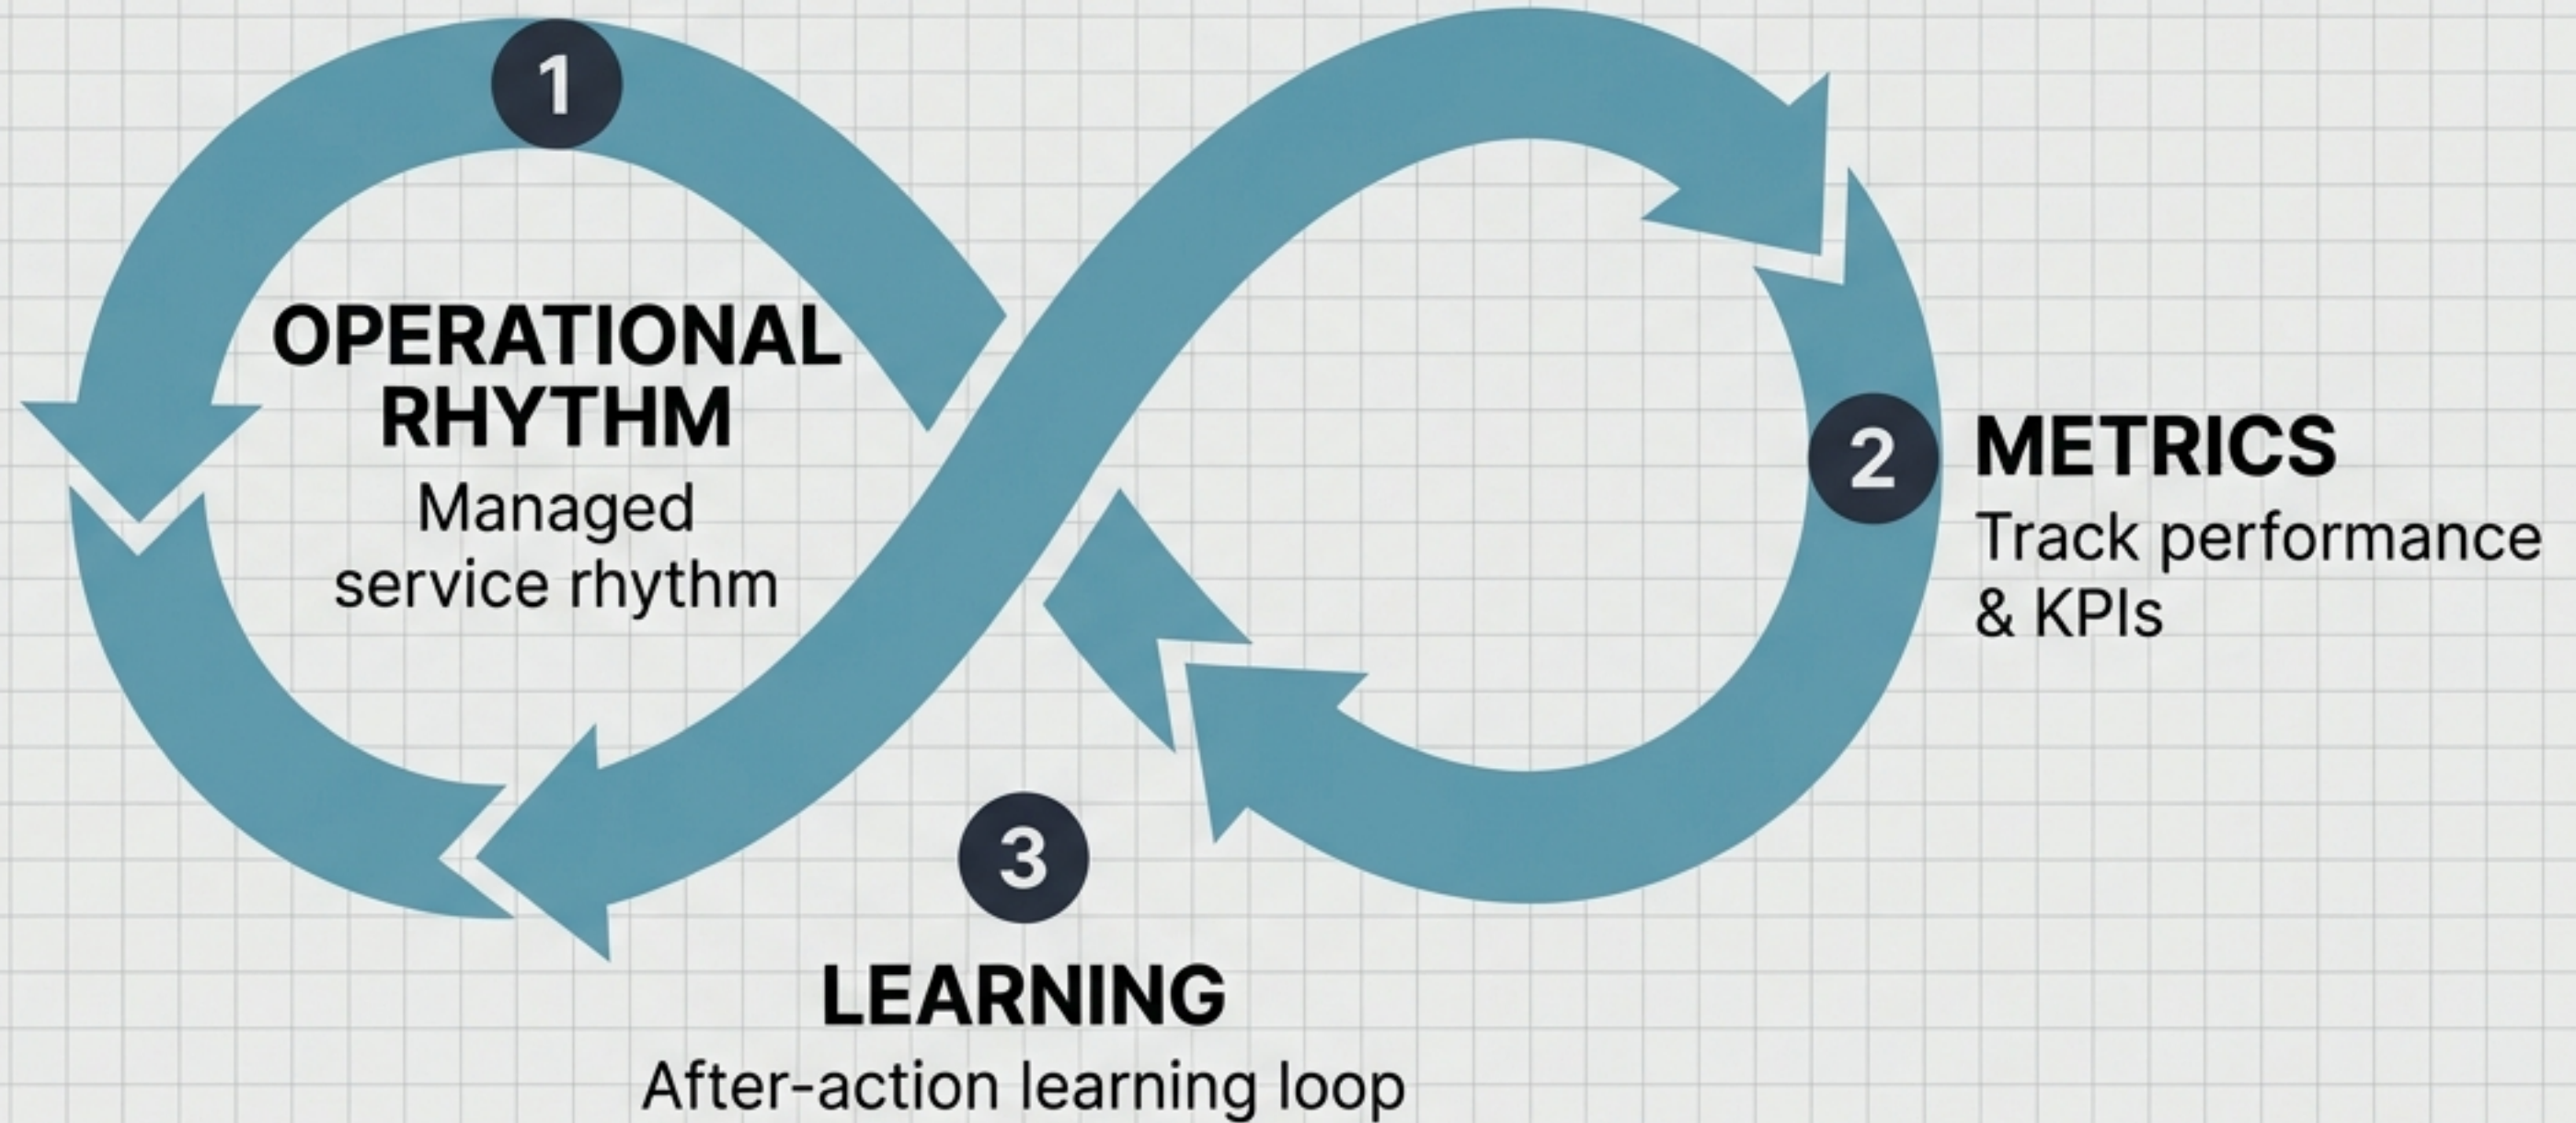

MARCH 15 IS THE BEGINNING OF THE OPTIMIZED RUN STATE.
